



SAP BTP COCKPIT
SAP CLOUD INTEGRATION

CAPSTONE PROJECT

Employee Data Synchronization

using SAP Integration Suite

DOCUMENT TYPE	Project Documentation & Evidence Pack
SCOPE	Implementation • Testing • Operations
PROJECT ID	P2012764983
PLATFORM	SAP Integration Suite / SAP Cloud Integration
TRAINER	Laxmi Ahuja

Prepared by **Mudavath Vinod**

Evidence Coverage

Integration Flows • Adapter Configurations • Mapping • SFTP • Mail • Exception Handling • Monitoring • Testing • Agile Delivery

INTEGRATION SOLUTIONS


-  Integration Flows
-  Adapter Configurations
-  Mapping
-  SFTP
-  Mail
-  Exception Handling
-  Monitoring
-  Testing
-  Agile Delivery



TABLE OF CONTENTS

SECTION	TITLE	PAGE
1	PROJECT OVERVIEW	4
2	USER STORIES	5
3	PRODUCT BACKLOG	6
4	SPRINT PLANNING	7
5	SPRINT BACKLOG	8
6	DAILY STAND-UP NOTES	9
7	SPRINT REVIEW	10
8	SPRINT RETROSPECTIVE	11
9	TECHNICAL DOCUMENTATION	14
10	TESTING DOCUMENTATION	15
11	TESTING	16
12	OUTPUT SCREENSHOTS	23
13	PROJECT SUMMARY	24

Document structure The document follows an Agile delivery structure and then provides technical implementation, testing, and evidence sections.

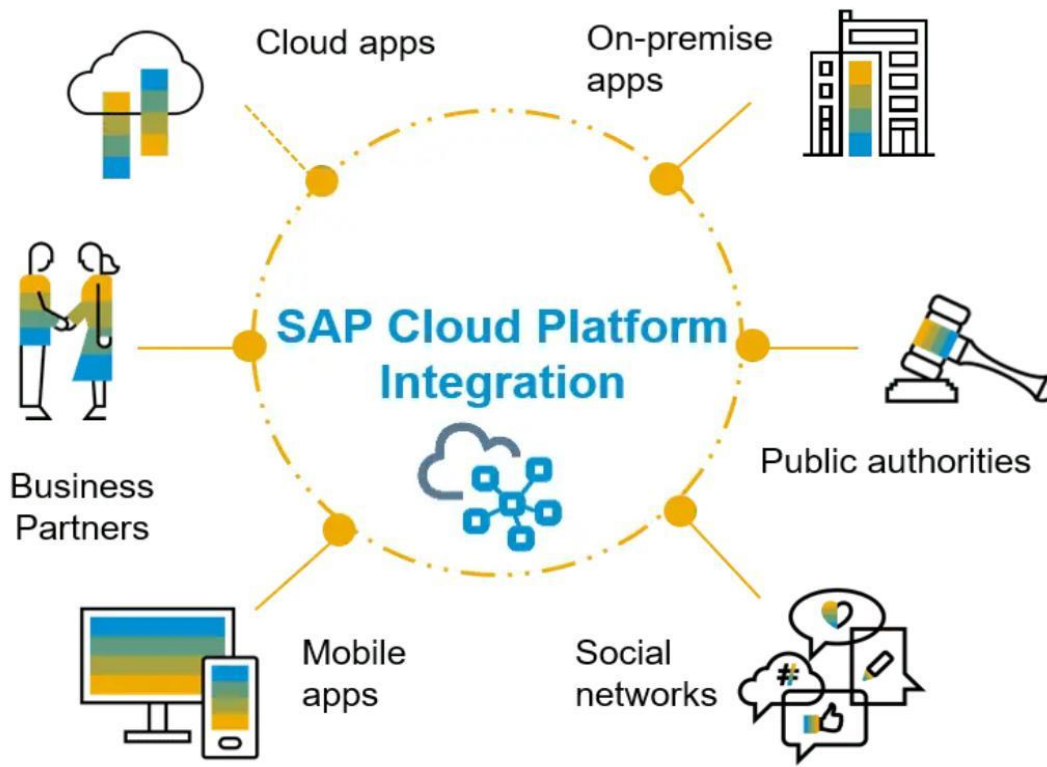

1. PROJECT OVERVIEW

Employee Data Synchronization using SAP Integration Suite

1.1 Problem Statement

Organizations frequently maintain employee information across multiple SAP and external systems. Manual transfer is time-consuming, inconsistent, and prone to human error. Employee data from SAP SuccessFactors must be retrieved, transformed, validated, and synchronized with SAP S/4HANA in the required target structure.

Processed information may also need to be converted into CSV and securely distributed through SFTP or communicated through email. Integration failures must be captured, made visible to administrators, and communicated to responsible users for timely corrective action.

Business Challenge Eliminate repetitive manual employee-data transfers while improving consistency, automation, secure distribution, error visibility, and operational monitoring.

1.2 Project Objective

Design and implement an automated employee-data integration solution using SAP BTP Cloud Integration (SAP Integration Suite). The solution retrieves employee information from SuccessFactors, transforms it for S/4HANA, processes the target record, generates CSV output, distributes it through SFTP and email, and handles failures through an Exception Subprocess.

#	OBJECTIVE AREA	TARGET OUTCOME
1	Automated Triggering	Scheduled Timer Start event
2	Employee Data Retrieval	Fetch required SuccessFactors employee information
3	Data Transformation	Map SuccessFactors data to S/4HANA structure
4	S/4HANA Synchronization	Create/process employee records
5	File Generation	Convert XML output to structured CSV
6	Secure Distribution	Transfer CSV through SFTP
7	Business Communication	Send required information/notifications by email
8	Error Management	Capture failures and notify responsible users
9	Operational Monitoring	Monitor successful and failed message processing


1.3 High-Level Integration Scope

TIMER → SUCCESSFACTORS ODATA V2 → CLOUD INTEGRATION → MESSAGE MAPPING → S/4HANA → XML/CSV → SFTP + EMAIL

Processing model Retrieve → Transform → Synchronize → Convert → Distribute

EMPLOYEE DATA SYNCHRONIZATION – INTEGRATION ARCHITECTURE

End-to-End Employee Data Integration using SAP Integration Suite



ARCHITECTURE OVERVIEW

STEP	COMPONENT
1	TIMER
2	SUCCESSFACTORS ODATA V2
3	CLOUD INTEGRATION
4	MESSAGE MAPPING
5	S/4HANA
6	XML / CSV
7	SFTP + EMAIL

KEY BENEFITS


- Automated & Scheduled Processing
- Accurate & Consistent Employee Data
- Secure File Transfer via SFTP
- Email Notifications & Alerts
- End-to-End Monitoring & Visibility

1.4 Expected Business Benefits

- Reduced manual effort through scheduled processing.
- Improved employee-data consistency across systems.
- Faster synchronization of employee master information.
- Standardized CSV output for file-based processing and reporting.
- Secure external file distribution through SFTP.
- Reliable communication through email notifications.
- Centralized error handling using an Exception Subprocess.
- Improved operational visibility through monitoring.

1.5 Scope Boundary

The project scope covers employee-data retrieval from SAP SuccessFactors, transformation and synchronization with SAP S/4HANA, XML-to-CSV conversion, SFTP and email distribution, exception handling, and integration monitoring. Business processes outside these integration activities are outside the primary scope unless explicitly required.

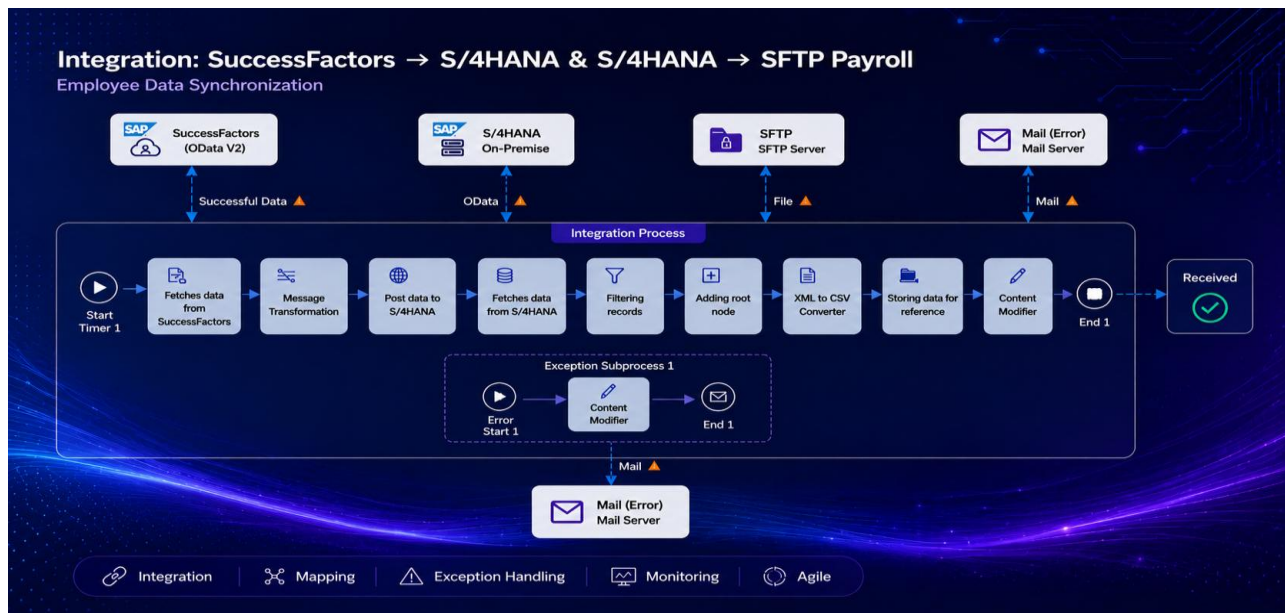

2. USER STORIES

Functional requirements are defined from the perspective of the stakeholders involved in employee-data retrieval, transformation, target integration, distribution, exception handling, and monitoring.

ID	PERSONA	REQUIREMENT	PRIORITY	ACCEPTANCE CRITERIA	COMPONENT	OUTCOME
US01	Integration Administrator	Automatic Timer execution	High	Scheduled start; no manual trigger; visible in monitoring	Timer Start Event	Automated execution
US02	HR / System User	Automatic SuccessFactors retrieval	High	Required fields retrieved; secure authentication	SuccessFactors OData V2	Latest employee data
US03	Integration Developer	Map employee fields to S/4HANA	High	Mandatory fields mapped and validated	Message Mapping	Correct target payload
US04	S/4HANA User	Create employee records automatically	High	Target service succeeds; response captured	S/4HANA OData	Synchronized records
US05	Integration Administrator	Retain/process successful data	High	Downstream payload available and traceable	Content Modifier / Processing	Processed employee data
US06	Business User	Convert XML to CSV	High	Headers and records generated correctly	XML-to-CSV Converter	Reusable CSV
US07	External System User	Secure CSV transfer via SFTP	High	Connection and file transfer succeed	SFTP Adapter	Secure delivery
US08	Business User	Send information/notifications by email	Medium	Content generated and delivered	Mail Adapter	Business communication
US09	Integration Administrator	Distribute through Sequential Multicast	Medium	Branches execute sequentially and are traceable	Sequential Multicast	Controlled multi-channel output
US10	System Administrator	Capture integration errors	High	Exceptions are caught with context	Exception Subprocess	Controlled failures
US11	System Administrator	Notify responsible users of failures	High	Error details are generated and sent	Exception + Mail	Timely notification
US12	Integration Administrator	Monitor complete iFlow execution	High	Status, failures and logs are traceable	MPL / Monitoring	Operational visibility

2.1 User Story Coverage Summary

CATEGORY	STORIES	COUNT	COVERAGE
Automation & Data Retrieval	US01–US02	2	Timer + SuccessFactors
Data Transformation & S/4HANA	US03–US05	3	Mapping + target processing
File & External Distribution	US06–US09	4	CSV + SFTP + Email + Multicast
Error Handling & Notifications	US10–US11	2	Exception + failure notification
Monitoring & Operations	US12	1	End-to-end monitoring

2.2 Definition of Done for User Stories

- Required configuration and security/credential artifacts are assigned.
- Positive testing is completed with valid employee data.
- Mandatory fields and transformation rules are validated.
- SFTP and email channels are tested where applicable.
- Exception handling is verified with a controlled failure.
- Message status and logs are checked in Cloud Integration Monitoring.
- Acceptance criteria are satisfied and evidence is captured.

3. PRODUCT BACKLOG

Status 8 backlog items • 7 High priority • 1 Medium priority • 100% Completed

3.1 Overview

The Product Backlog contains the prioritized requirements and implementation activities covering the complete integration lifecycle.


ID	BACKLOG ITEM	DELIVERABLE	PRIORITY	STATUS
PB01	SAP BTP & iFlow Setup	Environment, flow structure, connectivity	High	Completed
PB02	Fetch SuccessFactors Data	Employee master-data retrieval	High	Completed
PB03	Employee Data Mapping	Source-to-target transformation	High	Completed
PB04	Create S/4HANA Records	Target employee synchronization	High	Completed
PB05	XML-to-CSV Conversion	File-based output generation	High	Completed
PB06	SFTP & Email Distribution	Secure file and business communication	Medium	Completed
PB07	Exception Handling	Capture and notify integration failures	High	Completed
PB08	Testing & Deployment	Validate, fix and deploy solution	High	Completed

3.2 Backlog Prioritization

PRIORITY	MEANING	ITEMS
High	Core capability required for end-to-end integration	PB01, PB02, PB03, PB04, PB05, PB07, PB08
Medium	Supporting distribution and communication	PB06

3.3 Product Backlog Delivery Flow

SETUP → RETRIEVE → MAP → CREATE → CONVERT → DISTRIBUTE → HANDLE ERRORS → TEST & DEPLOY

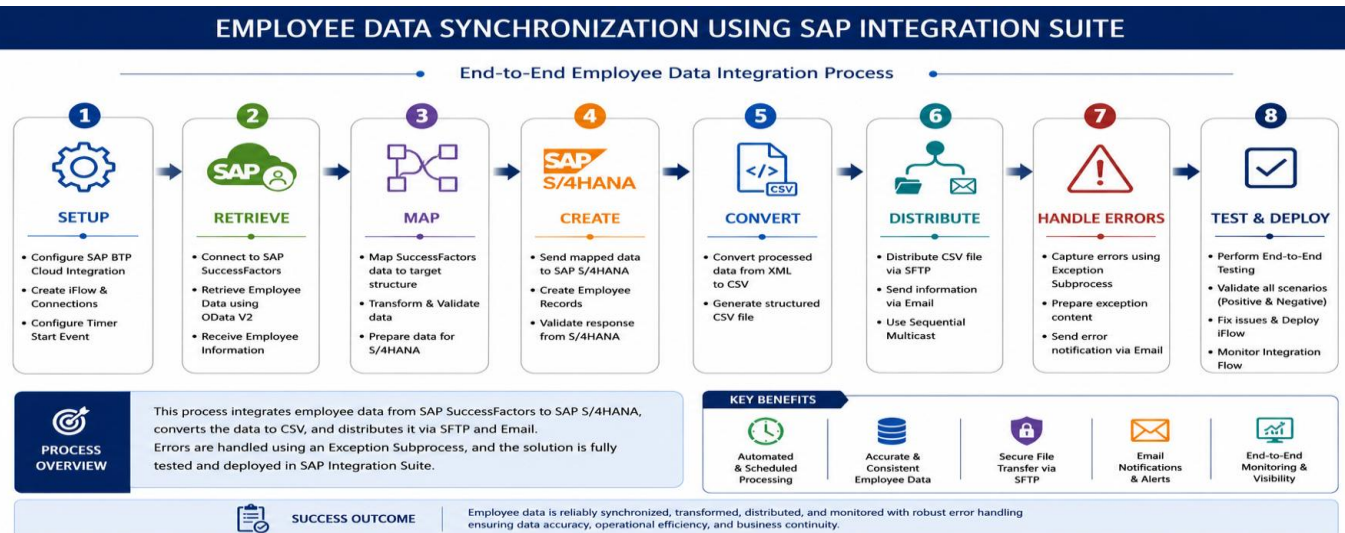

3.4 Definition of Done

- ✓ Implemented
- ✓ Configured
- ✓ Validated
- ✓ Tested
- ✓ Defects resolved
- ✓ Output verified
- ✓ Deployment ready

4. SPRINT PLANNING

The project is divided into five focused sprints. Each sprint has a clear goal, implementation activities, and an expected outcome.

Sprint 1 – Environment Setup & iFlow Creation

Sprint Goal Environment Setup & iFlow Creation

- Configure Cloud Integration
- Create package and iFlow
- Configure Timer Start
- Configure SuccessFactors connection
- Deploy initial iFlow

Expected Outcome Basic timer-driven flow connected to SuccessFactors.

Sprint 2 – SuccessFactors Retrieval & Mapping

Sprint Goal SuccessFactors Retrieval & Mapping

- Fetch employee information
- Analyze source XML
- Create source-to-target mapping
- Map Employee ID, Name, Country and City
- Validate output

Expected Outcome Employee data transformed into the required S/4HANA structure.

Sprint 3 – S/4HANA Integration & Employee Storage

Sprint Goal S/4HANA Integration & Employee Storage

- Configure S/4HANA receiver
- Configure OData/API communication
- Send mapped data
- Create employee records
- Validate response and storage
- Test success/failure scenarios

Expected Outcome Employee records successfully created and stored in S/4HANA.

Sprint 4 – XML-to-CSV & File Distribution

Sprint Goal XML-to-CSV & File Distribution

- Configure XML-to-CSV
- Generate CSV
- Configure Sequential Multicast
- Configure SFTP branch
- Configure SMTP/Mail branch
- Verify both outputs

Expected Outcome CSV generated and distributed through SFTP and email.

Sprint 5 – Exception Handling, Testing & Deployment

Sprint Goal Exception Handling, Testing & Deployment

- Create Exception Subprocess
- Configure Error Start
- Capture exception information
- Configure error email
- Run end-to-end tests
- Fix defects
- Deploy and monitor

Expected Outcome Tested and deployed solution with controlled error handling.

5. SPRINT BACKLOG

5.1 Overview

The **Sprint Backlog** is the set of development activities selected from the Product Backlog for implementation during each Agile Sprint. It provides a structured execution plan by dividing the overall integration project into smaller, manageable delivery increments.

For this project, the Sprint Backlog follows the complete integration lifecycle, starting with SAP BTP and iFlow setup and progressing through SuccessFactors data retrieval, data mapping, S/4HANA integration, file conversion, external distribution, exception handling, testing, and deployment.

Each sprint has a defined **goal, key delivery activities, and expected outcome**. This approach enables incremental development, continuous validation, and controlled delivery of the integration solution.

5.2 Sprint Execution Approach

The project was divided into **five implementation sprints**:

Setup → Retrieve → Map → Integrate → Distribute → Handle Errors → Test & Deploy

5.3 Sprint Backlog Characteristics

The Sprint Backlog provides the following benefits within the project:

- **Incremental Delivery** – The integration solution is developed in smaller functional increments.
- **Clear Ownership** – Each sprint has a defined implementation objective.
- **Progress Tracking** – Completed activities can be monitored throughout development.
- **Early Validation** – Integration issues can be identified before final deployment.
- **Controlled Development** – Technical dependencies are handled in a logical sequence.
- **Continuous Improvement** – Sprint reviews and retrospectives provide opportunities to improve subsequent activities.
- **End-to-End Traceability** – Each sprint contributes directly to the final integration solution.

5.4 Delivery Status

All planned sprint deliverables have been completed successfully.

SPRINT	KEY DELIVERY	STATUS
Sprint 1	Configure BTP, create iFlow and Timer	Completed
Sprint 2	Fetch SuccessFactors data and perform mapping	Completed
Sprint 3	Create records in S/4HANA and process employee data	Completed
Sprint 4	Convert XML to CSV and configure SFTP/Email	Completed
Sprint 5	Exception handling, testing and deployment	Completed

Delivery status All planned sprint deliverables are completed.

6. DAILY STAND-UP NOTES

6.1 Overview

Daily Stand-up is a short Agile progress-tracking activity used to monitor the day-to-day execution of the project. It provides visibility into **completed work, current activities, and blockers** that may affect the planned sprint objectives.

For this project, daily stand-up activities were used to track the incremental development of the **SAP Integration Suite employee-data integration flow**. The discussions focused on configuration, connectivity, data retrieval, mapping, S/4HANA processing, file conversion, and output-channel configuration.

6.2 Purpose of Daily Stand-ups

The daily stand-up process supports the project by providing:

- **Progress Visibility** – Tracks completed integration activities.
- **Daily Planning** – Identifies the work planned for the current day.
- **Blocker Identification** – Highlights configuration, mapping, or connectivity issues.
- **Early Issue Resolution** – Allows technical problems to be addressed before they impact later activities.
- **Sprint Alignment** – Ensures daily work contributes toward the sprint objective.
- **Continuous Tracking** – Maintains a clear development history throughout implementation.

6.3 Daily Progress Flow

COMPLETED WORK

↓

CURRENT WORK

↓

BLOCKER IDENTIFICATION

↓

ISSUE RESOLUTION

↓

NEXT DEVELOPMENT ACTIVITY

6.4 Stand-up Tracking Areas

Completed Records the integration activities completed during the previous working period.

Current Work Defines the activity currently being implemented or validated.

Blockers Captures technical issues, configuration problems, mapping issues, or dependencies affecting progress.

Resolution Ensures identified blockers are addressed before they impact subsequent activities.

6.5 Daily Stand-up Summary

The project stand-ups progressed from **SAP BTP environment setup** through **SuccessFactors connectivity, employee-data retrieval, mapping, S/4HANA processing, XML-to-CSV conversion, and output-channel configuration**.

DAY	COMPLETED	CURRENT WORK	BLOCKERS
Day 1	BTP environment, package and basic iFlow configured	Timer + SuccessFactors connection	No blockers
Day 2	Timer and SuccessFactors connection configured	Fetch and validate employee payload	No blockers
Day 3	Employee data fetched; source-to-target mapping prepared	Complete S/4HANA mapping	Minor mapping issues
Day 4	Mapping validated; S/4HANA connection configured	Send mapped data and create records	No blockers
Day 5	S/4HANA processing completed; XML-to-CSV started	Sequential Multicast + SFTP + Email	No blockers

7. SPRINT REVIEW

7.1 Overview

The Sprint Review is an Agile Scrum activity conducted at the end of each sprint to evaluate the completed work, demonstrate the developed functionality, identify improvements, and confirm that the project is progressing according to the requirements.

In the **Employee Data Synchronization using SAP Integration Suite** project, Sprint Reviews were conducted after each development iteration. Each sprint focused on a specific stage of the integration, starting from the SAP BTP environment setup and progressing through SuccessFactors integration, data mapping, S/4HANA integration, SFTP and Mail distribution, exception handling, testing, and deployment.

The Sprint Review helped ensure that every component was successfully completed and integrated with the previously developed components. It also provided an opportunity to identify and resolve issues before moving to the next sprint.

7.2 Sprint-wise Review

Sprint 1: The SAP BTP environment, integration package, basic iFlow, and Timer Start event were configured, establishing the foundation of the integration solution.

Sprint 2: SuccessFactors connectivity was completed and employee data was retrieved. Source-to-target mapping was implemented to transform the employee information into the required structure.

Sprint 3: SAP S/4HANA integration was completed. The transformed employee data was successfully sent to the target system and employee records were created.

Sprint 4: XML-to-CSV conversion was implemented. Sequential Multicast was configured to distribute employee data through SFTP and Mail channels.

Sprint 5: Exception Subprocess and error notification were implemented. End-to-end testing was completed, and the final integration solution was successfully deployed.

7.3 Sprint Review Summary

SPRINT	REVIEW HIGHLIGHT	RESULT
Sprint 1	BTP environment, package, iFlow and Timer Start were configured.	Basic integration flow created.
Sprint 2	SuccessFactors retrieval and source-to-target mapping were implemented.	Employee data transformed successfully.
Sprint 3	S/4HANA integration and employee record creation were completed.	Target records created successfully.
Sprint 4	XML-to-CSV conversion and Sequential Multicast with SFTP and Mail were completed.	Employee data distributed through both channels.
Sprint 5	Exception Subprocess, error notification, end-to-end testing and deployment were completed.	Final solution tested, deployed and protected by error handling.

7.4 Outcome

The Sprint Reviews confirmed the successful incremental development of the integration solution. By the end of Sprint 5, the complete employee synchronization process was implemented, tested, deployed, and supported with appropriate error-handling and notification mechanisms.

8. SPRINT RETROSPECTIVE

8.1 Overview

The Sprint Retrospective is an Agile Scrum activity conducted after each sprint to evaluate the development process, identify what went well, recognize improvement areas, and define corrective actions for future sprints. It helps the team continuously improve the quality, efficiency, and reliability of the project.

For the **Employee Data Synchronization using SAP Integration Suite** project, retrospectives were used to review technical configuration, data mapping, integration testing, error handling, and deployment activities. The feedback from each sprint was used to improve the activities in the following sprint.

8.2 Sprint Retrospective Summary

SPRINT	WHAT WENT WELL	IMPROVEMENT AREA	ACTION
Sprint 1	BTP, iFlow and Timer setup succeeded.	Configuration took additional time.	Prepare connection details and checklist.
Sprint 2	Retrieval and mapping succeeded.	Some fields needed validation.	Prepare sample payloads earlier.
Sprint 3	S/4HANA connection and record creation succeeded.	More negative tests were possible.	Include invalid-data scenarios.
Sprint 4	CSV conversion and multi-channel output succeeded.	CSV validation needed more testing.	Validate CSV and test branches independently.
Sprint 5	Exception handling, notifications, testing and deployment succeeded.	Error scenarios could start earlier.	Introduce exception testing from development start.


8.3 Overall Outcome

The Sprint Retrospectives helped identify process and technical improvements throughout the project. Early preparation of connection details, sample payload validation, negative testing, CSV validation, and early exception testing improved the reliability of the integration solution. These continuous improvements contributed to the successful completion, testing, and deployment of the final solution.

9. TECHNICAL DOCUMENTATION

9.1 Project Architecture

The solution uses SAP BTP Cloud Integration as the middleware layer between SuccessFactors, S/4HANA, SFTP and email. The flow retrieves employee data, transforms it, processes the target record, converts the processed data to CSV, and distributes the output.

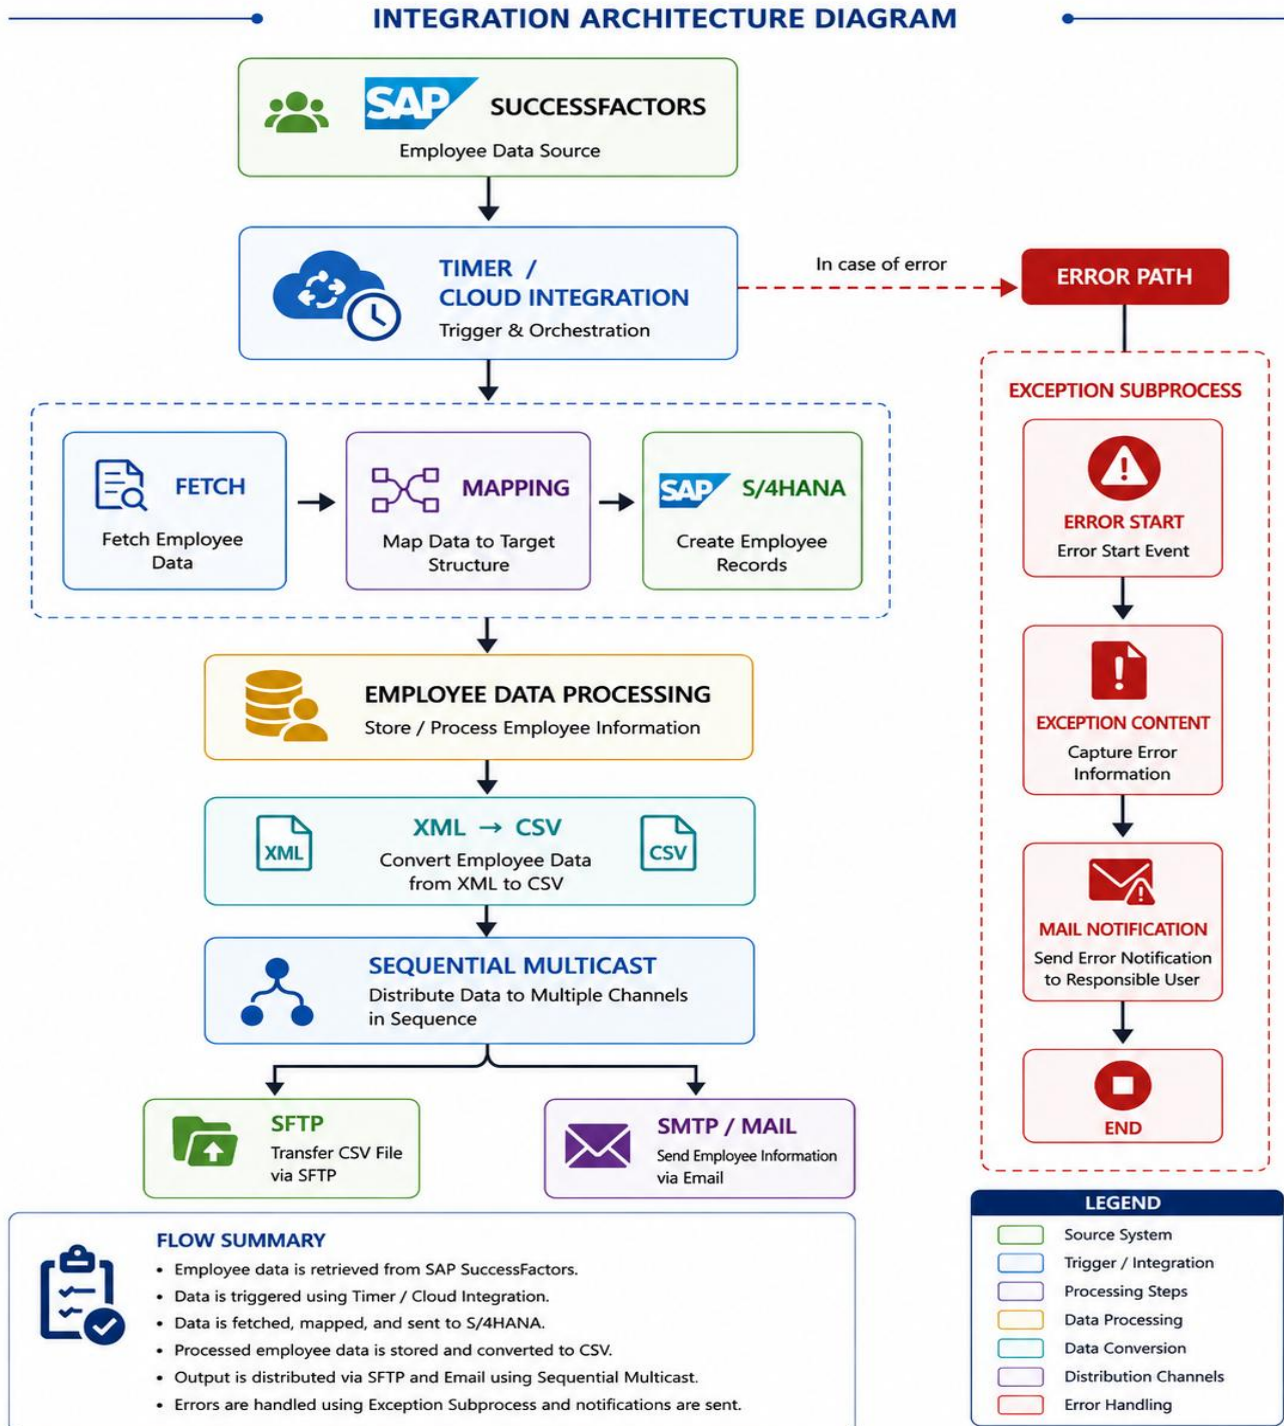

9.2 SAP BTP Cloud Integration

SAP BTP Cloud Integration provides the middleware capabilities for communication, transformation, routing, monitoring, and exception handling. It centralizes processing between the source, target, file, and communication channels.

9.3 Timer Start Event

The Timer Start event initiates the iFlow automatically according to the configured schedule.

- Automatically trigger the iFlow
- Retrieve employee information periodically
- Reduce manual intervention

Evidence Insert Timer Start configuration screenshot here.

9.4 Fetching SF Data

The SuccessFactors connection retrieves employee information and passes the employee payload to the mapping step.

TARGET FIELD	PURPOSE
Mandt	Client / target context
Participantid	Employee / participant identifier
Country	Employee country
Sfempname	Employee name
City	Employee city

Evidence Insert SuccessFactors retrieval configuration or message-processing screenshot here.

9.5 Mapping SF to S/4HANA

The mapping step transforms the SuccessFactors source structure into the target structure required for S/4HANA processing.

SOURCE	TARGET
Mandt	Mandt
Participant ID	Participantid
Country	Country
Employee Name	Sfempname
City	City

Evidence Insert mapping configuration screenshot here.

9.6 Creating Record in S/4HANA

The mapped employee information is sent to S/4HANA through the configured receiver. The target system processes the payload and creates the required employee record.

- Send transformed employee data
- Create employee records
- Validate target response

Expected Result Employee record is successfully created in S/4HANA.

Employee Data Storing: The processed employee information is retained/forwarded in the required structure for downstream processing and output generation.

9.7 XML to CSV Converter

The XML-to-CSV Converter changes processed employee information into a structured CSV file for file-based exchange and reporting.

XML FIELD	CSV COLUMN	SAMPLE
Mandt	Mandt	500
Participantid	Participantid	EMP001
Country	Country	India
Sfempname	Sfempname	Harrison Skou
City	City	Chennai

9.8 Sequential Multicast

Sequential Multicast distributes the processed output through the configured channels in sequence.

BRANCH	FUNCTION	EXPECTED RESULT
SFTP	Transfer generated CSV to external server	File delivered successfully
SMTP / Mail	Send employee information or notification	Email delivered successfully


Evidence Insert SFTP receiver/output screenshot and successful email screenshot here.

9.9 Exception Subprocess

The Exception Subprocess handles errors that occur during integration processing.

ERROR START → EXCEPTION CONTENT → MAIL NOTIFICATION → EXCEPTION END

EXCEPTION SUBPROCESS FLOW

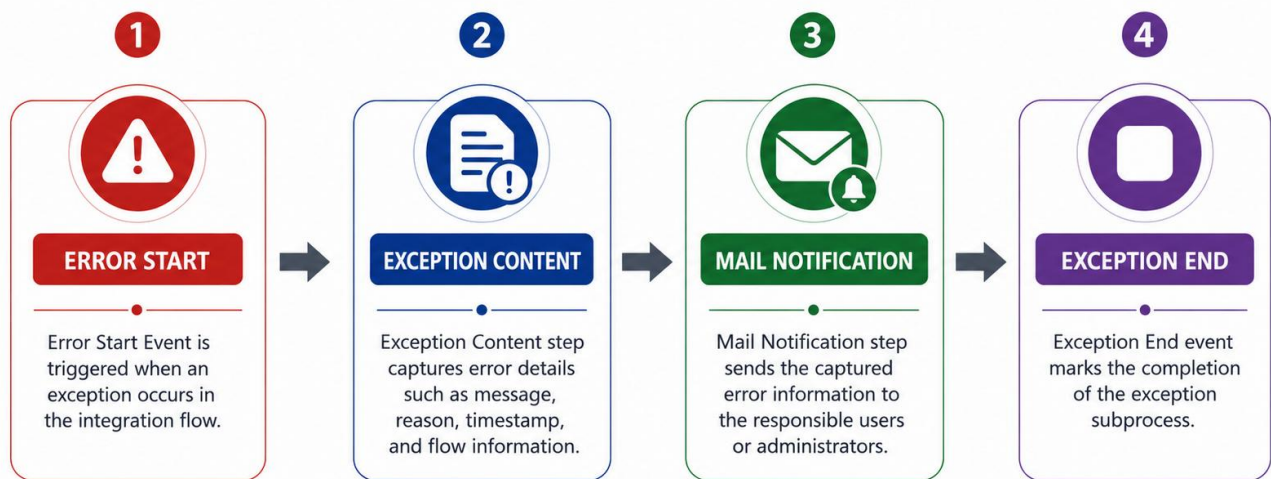

PURPOSE

This subprocess ensures that all integration errors are captured, documented, and notified to the appropriate users for quick resolution.

9.10 Exception Content & End Events

Exception Content prepares failure information such as error message, reason, flow information, processing details, and failure context.

END EVENT	MEANING
SFTP End	Successful completion of SFTP branch
Mail End	Successful completion of email branch
Exception End	Completion of error handling after notification

10. TESTING DOCUMENTATION

Testing verifies that every integration component works correctly and that employee data moves from source to target and output channels as expected.

10.1 Testing Overview

Testing verifies that every component of the **Employee Data Synchronization using SAP Integration Suite** solution works correctly and that employee data is transferred accurately from the source system to the target system and configured output channels. Functional testing was performed across the complete integration flow, including data retrieval, transformation, S/4HANA processing, CSV generation, SFTP transfer, email notification, and exception handling.

ID	TEST SCENARIO	EXPECTED RESULT	STATUS
TC01	Timer trigger	iFlow starts successfully	Pass
TC02	SuccessFactors retrieval	Employee data retrieved	Pass
TC03	Payload validation	Correct employee information received	Pass
TC04	Field mapping	Source fields mapped correctly	Pass
TC05	S/4HANA transfer	Data reaches S/4HANA	Pass
TC06	Employee record creation	Record created successfully	Pass
TC07	Employee processing/storage	Data processed correctly	Pass
TC08	XML-to-CSV	Valid CSV generated	Pass
TC09	Sequential Multicast	Data routed to branches	Pass
TC10	SFTP transfer	CSV reaches SFTP	Pass
TC11	Email output	Email delivered	Pass
TC12	Integration error	Exception Subprocess activated	Pass
TC13	Exception content	Error captured correctly	Pass
TC14	Error notification	Notification sent by email	Pass
TC15	End-to-end execution	Complete flow executes successfully	Pass

10.2 Test Result

A total of **15 functional test cases** were executed covering the complete integration lifecycle. All **15 out of 15 test cases passed successfully**, resulting in a **100% functional test pass rate**. The testing confirmed that the integration flow performs employee data synchronization, multi-channel distribution, and exception handling as expected.

Test result 15 / 15 functional test cases passed.

11. TESTING

11.1 Integration Testing

Integration testing validates the communication, connectivity, and data exchange between the systems involved in the Employee Data Synchronization solution. Each integration point was tested to ensure that employee information is successfully retrieved, transformed, transferred, and delivered through the configured output channels.

INTEGRATION POINT	VALIDATION
SuccessFactors → Cloud Integration	Employee data retrieved successfully
Cloud Integration → S/4HANA	Mapped employee data sent successfully
Cloud Integration → SFTP	Generated CSV transferred successfully
Cloud Integration → SMTP	Configured email delivered successfully

The integration testing confirmed that all major system interfaces were functioning as expected and that data could successfully flow through the complete integration architecture.

11.2 Negative Testing

Negative testing verifies controlled behavior when failures occur.

- Invalid employee data
- Missing mandatory fields
- Incorrect mapping
- S/4HANA connection failure
- SuccessFactors connection failure
- Invalid target response
- SFTP connection failure
- Email delivery failure

Expected behavior Exception Subprocess captures the failure and generates the appropriate notification.

11.3 Defects and Fixes

ID	DEFECT	IMPACT	RESOLUTION	STATUS
BUG01	Incorrect employee field mapping	Incorrect target data	Corrected field mapping.	Fixed
BUG02	Data format mismatch	Target processing failure	Corrected transformation.	Fixed
BUG03	Invalid employee payload	Processing failure	Added validation and error handling.	Fixed
BUG04	CSV output format issue	Incorrect file generation	Corrected XML-to-CSV configuration.	Fixed
BUG05	Exception not notified	Slow failure identification	Configured Exception Subprocess + email.	Fixed
BUG06	Output channel issue	File/email not delivered	Corrected receiver configuration.	Fixed

11.4 Final Testing Result


The complete employee integration flow was tested from the Timer Start event through SuccessFactors retrieval, mapping, S/4HANA processing, XML-to-CSV conversion, Sequential Multicast, SFTP transfer, and email output. Exception handling was also tested to verify failure capture and notification.

Final Result The implemented solution successfully meets the defined project requirements for automated employee data integration and distribution using SAP BTP Cloud Integration.

12. OUTPUT SCREENSHOTS


The following evidence points should be included in the final project pack. Replace each placeholder with the corresponding implementation or testing screenshot.

Figure 1
SAP BTP Cloud Integration iFlow

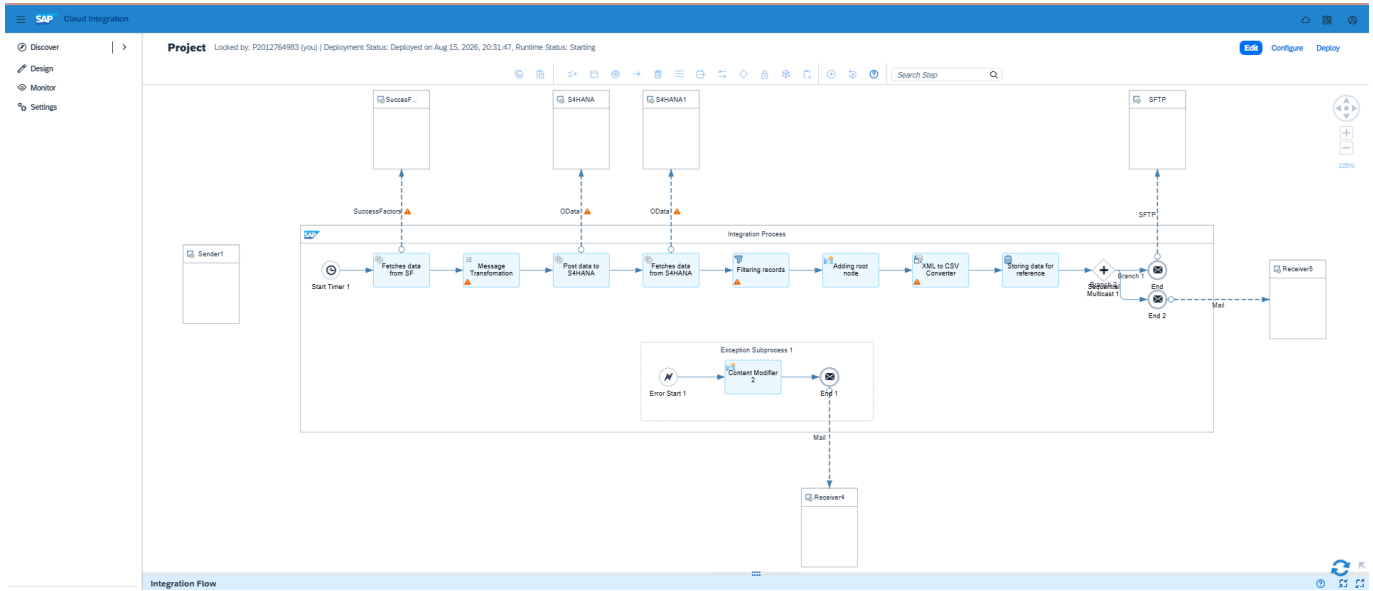


Complete integration flow for employee data processing.

Figure 2
SuccessFactors Data Retrieval

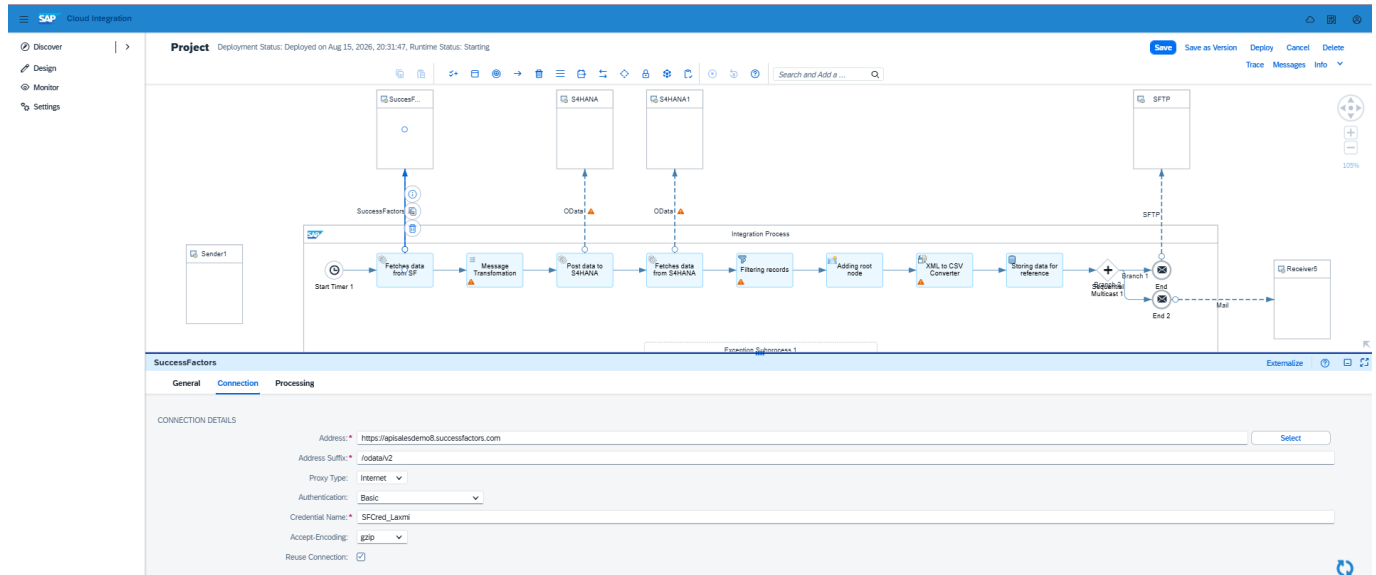


Employee data retrieval from SAP SuccessFactors.

Figure 3
Mapping

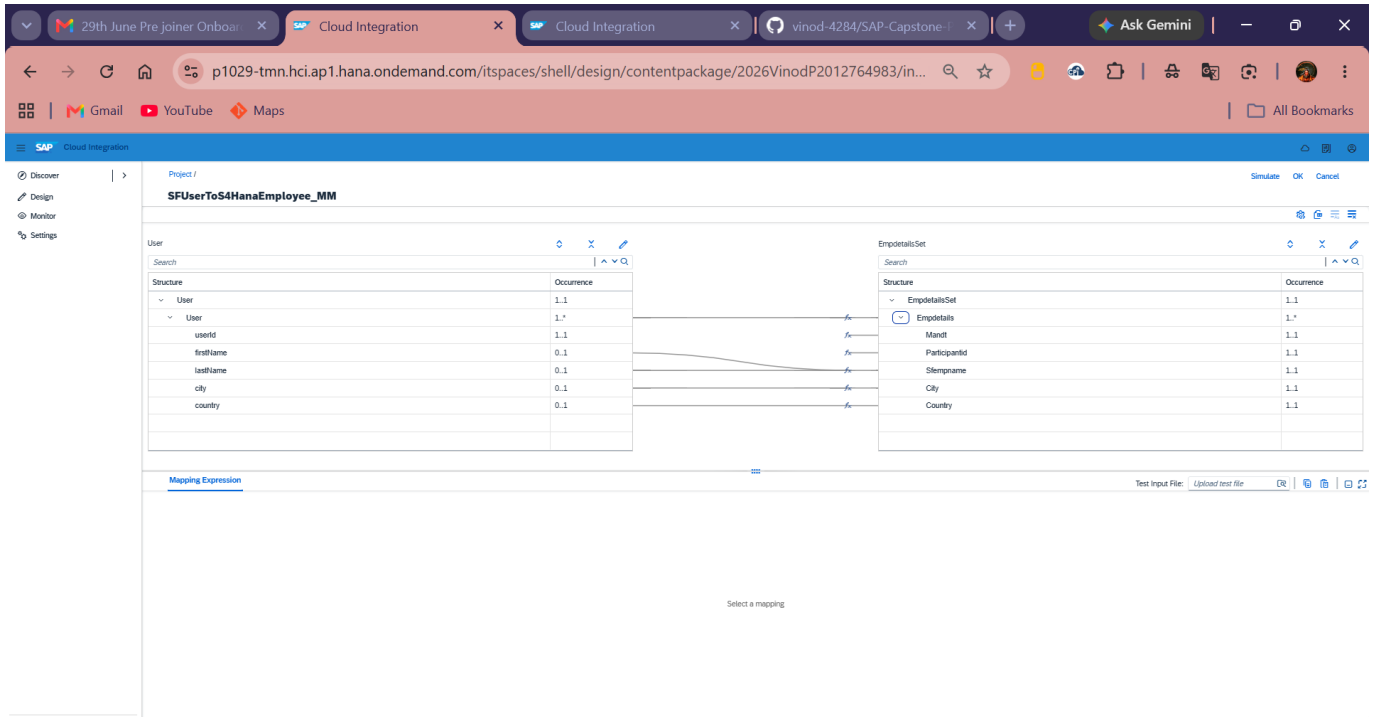


SuccessFactors employee data mapped to S/4HANA target structure.

Figure 4
S/4HANA Record Creation

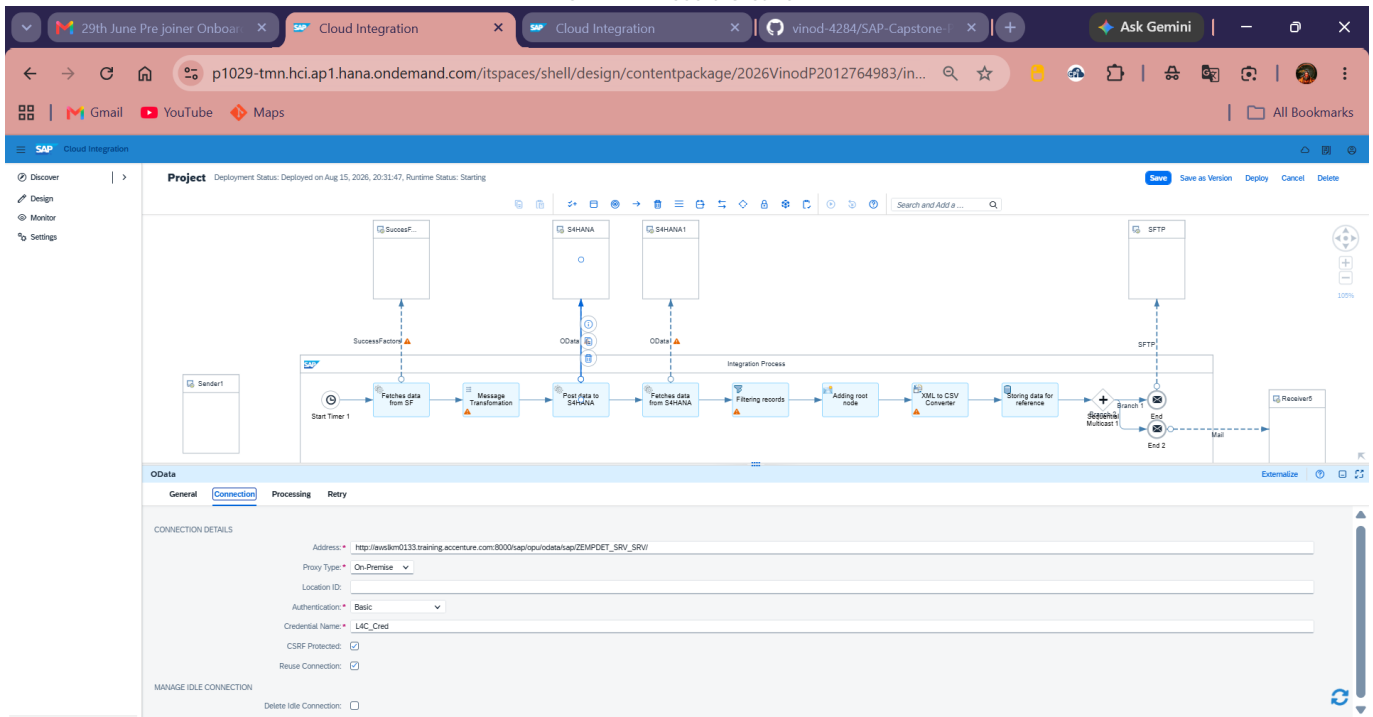


S/4HANA receiver and successful target response.

Figure 5
Employee Data

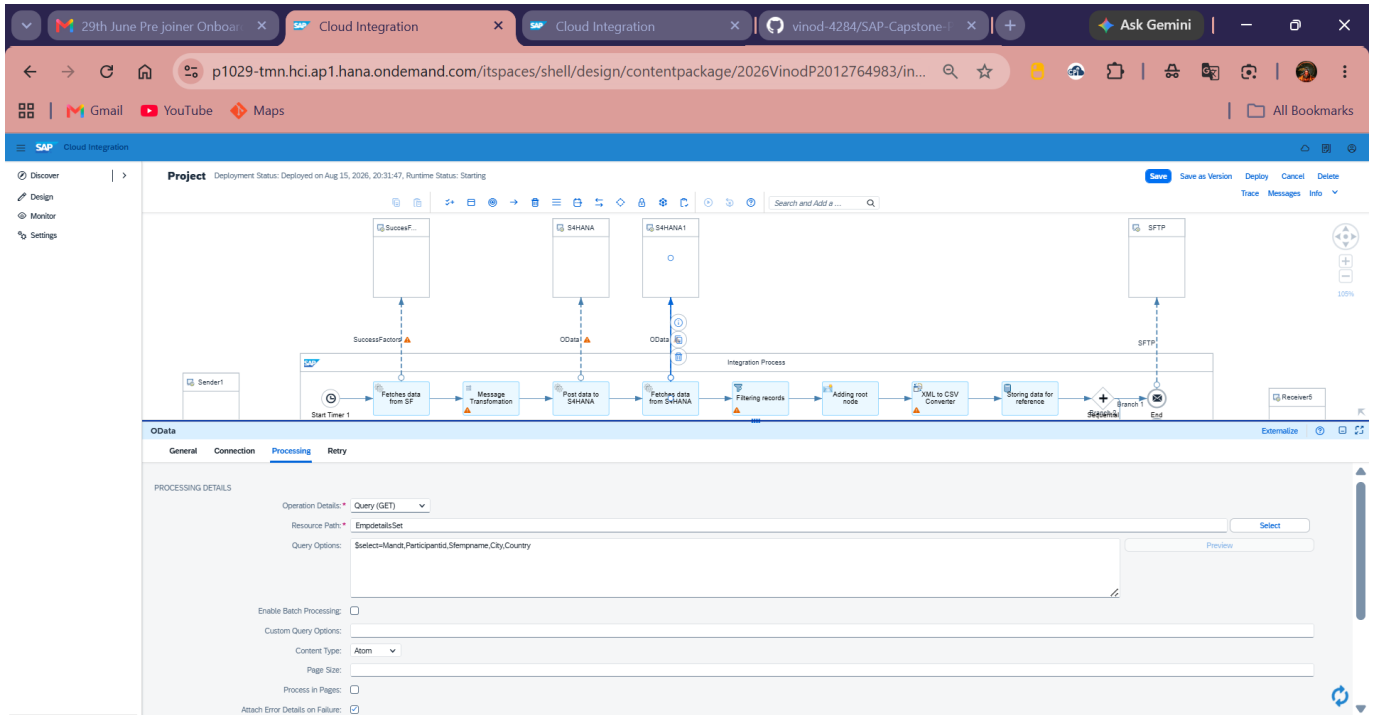


Processed employee data.

Figure 6
XML to CSV Conversion

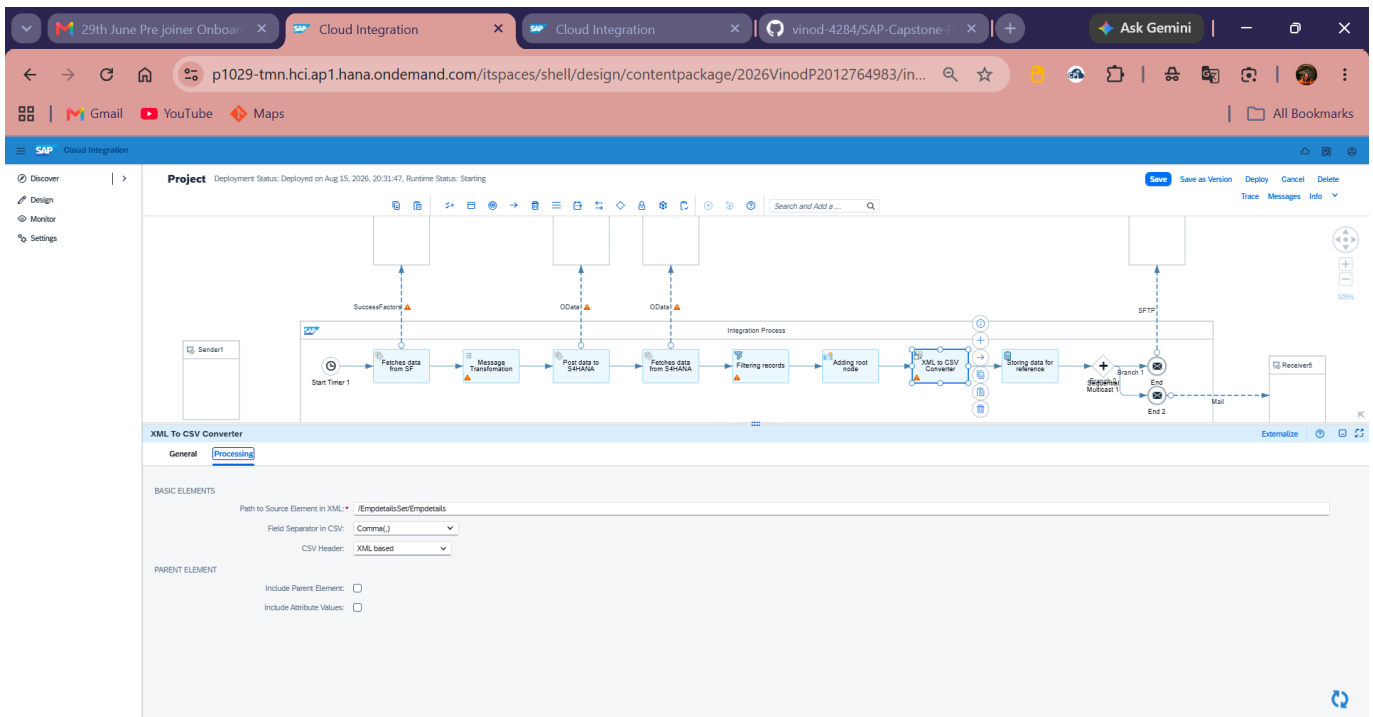


Conversion of employee data from XML to CSV.


Figure 7
SFTP Output

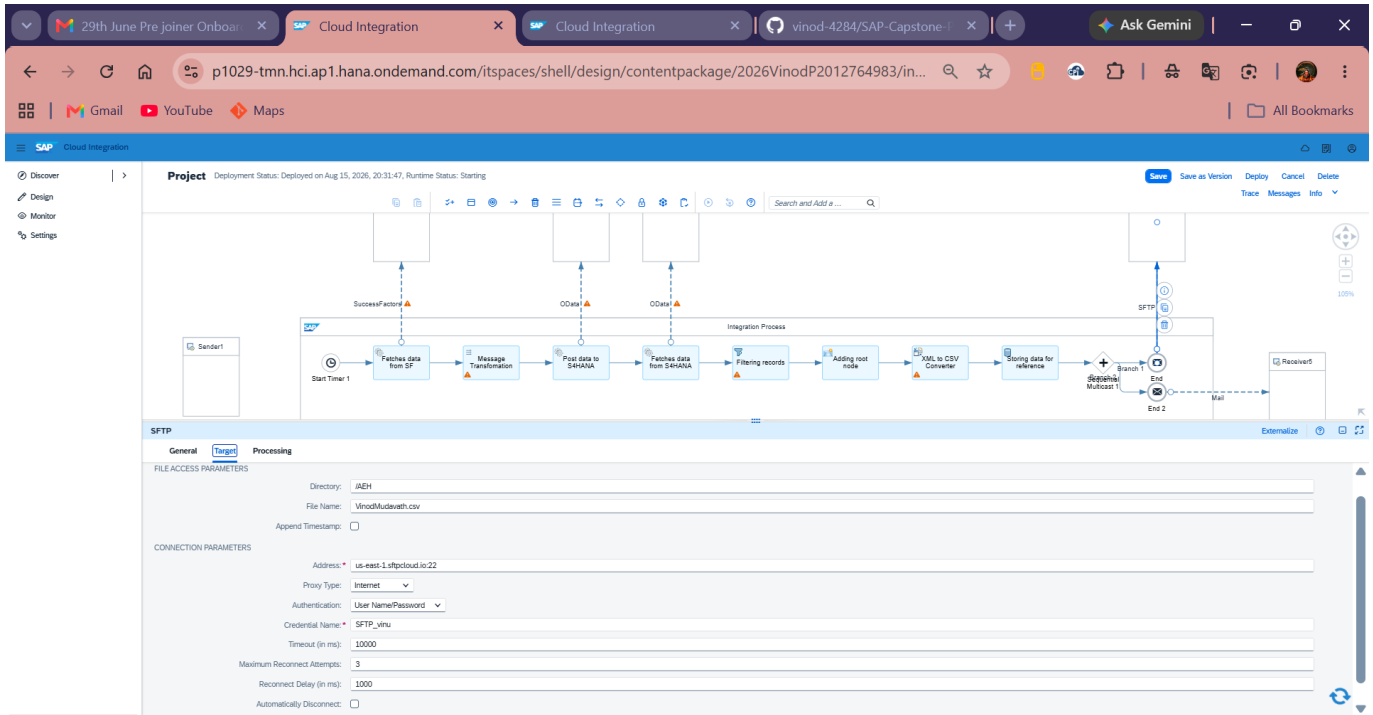

Successful transfer of employee CSV through SFTP.


Figure 8
Email Output

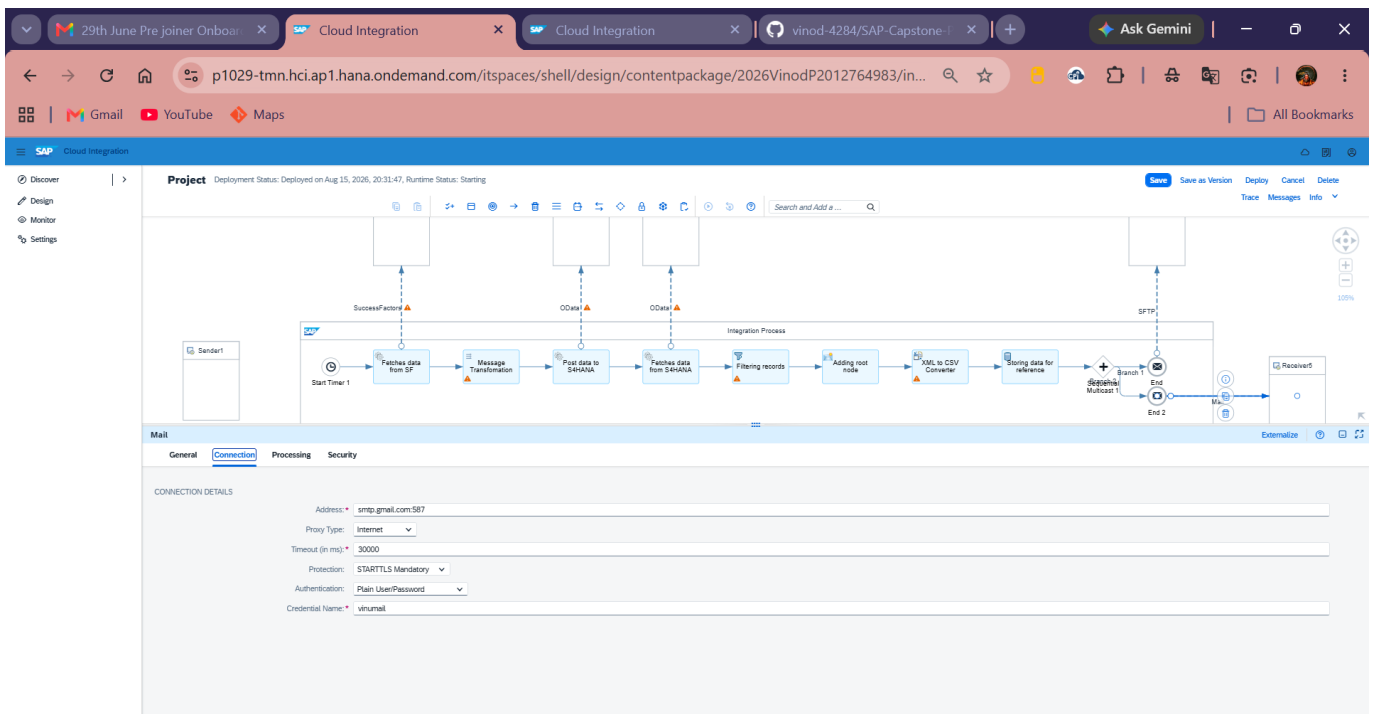

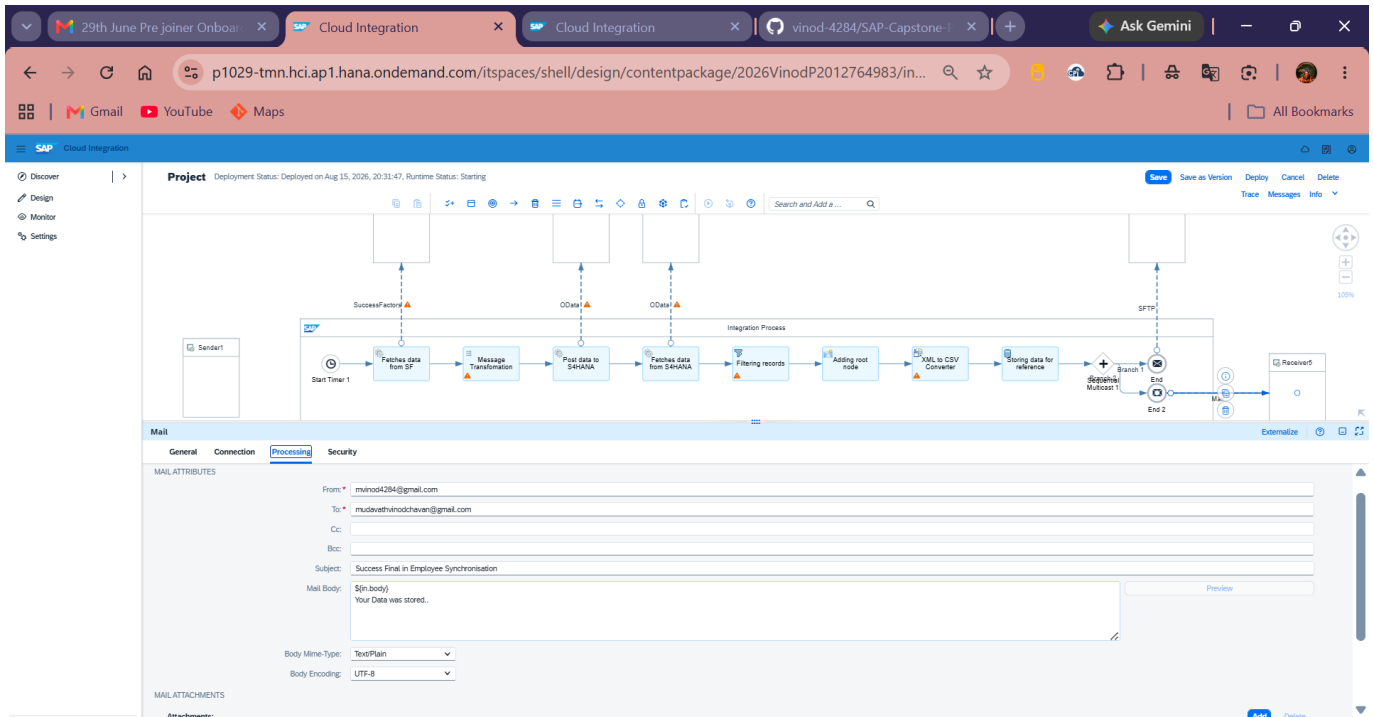

Successful email notification/output.

Figure 9
Exception Subprocess

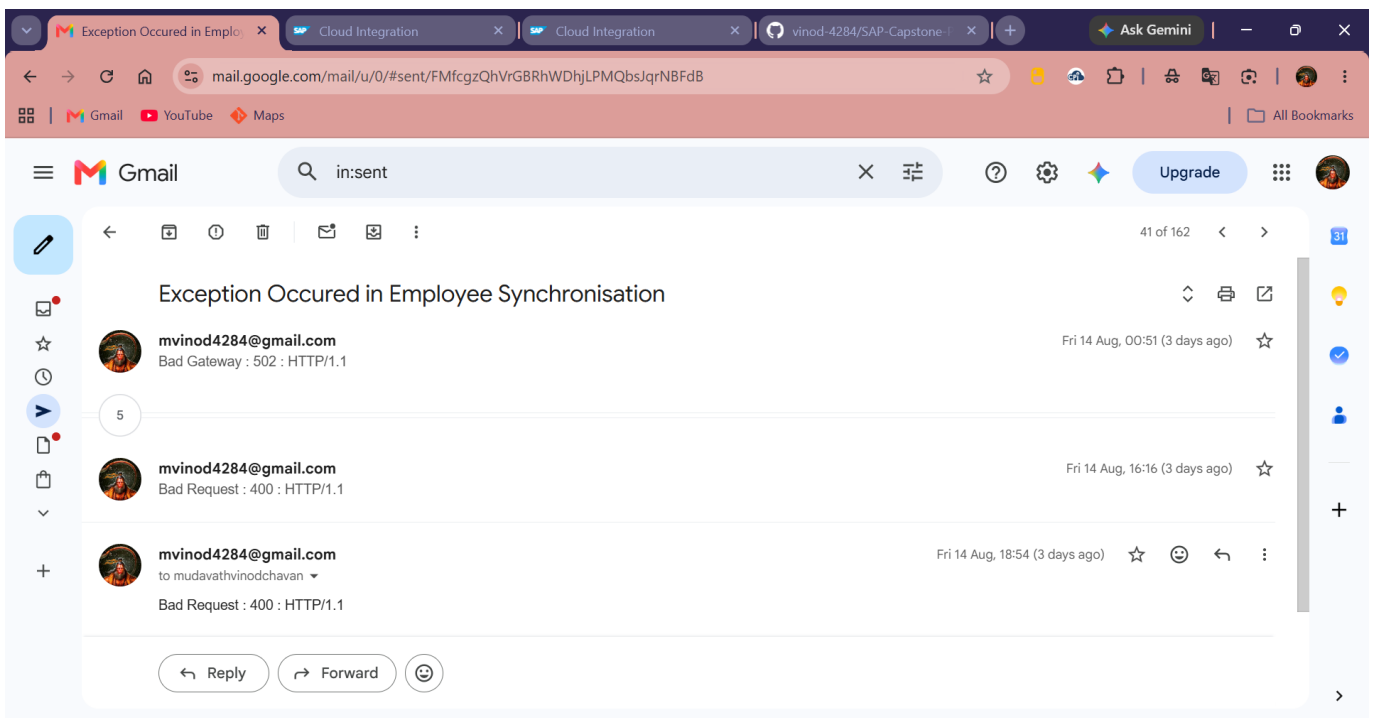



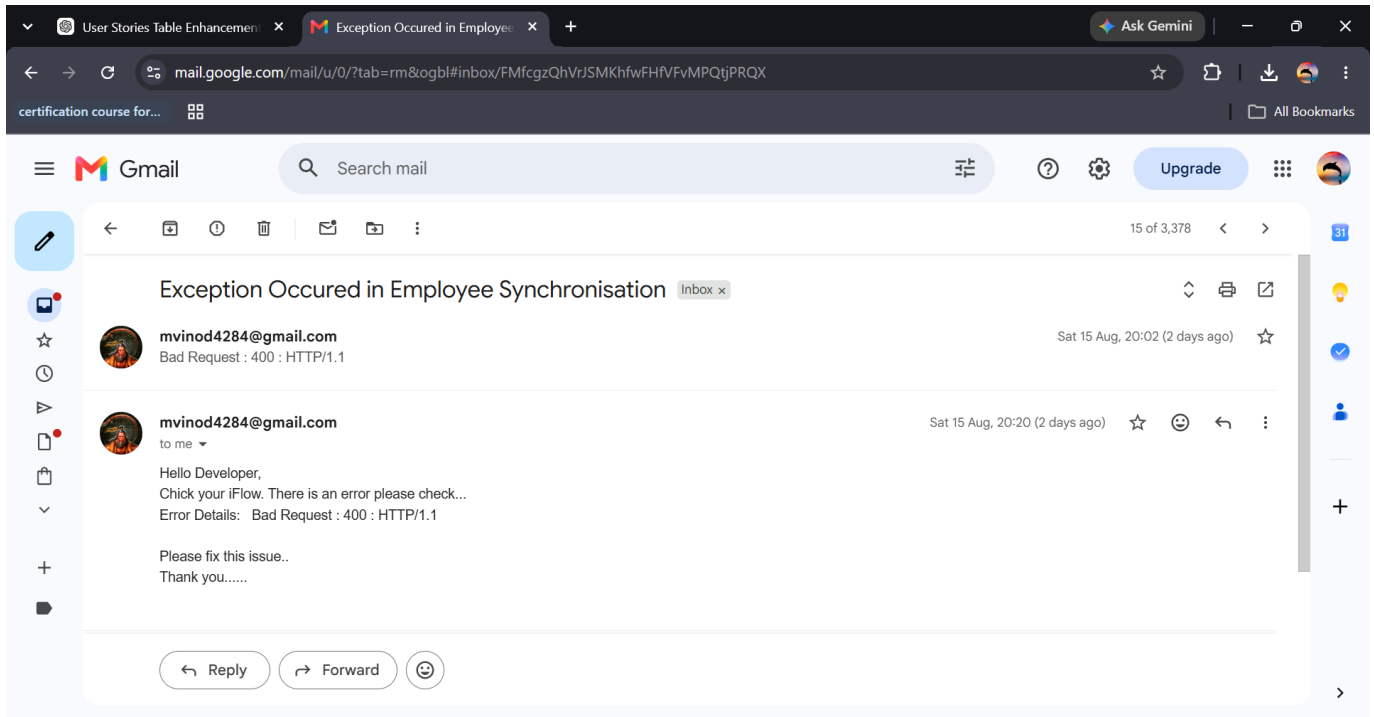


Figure 10
Output Target

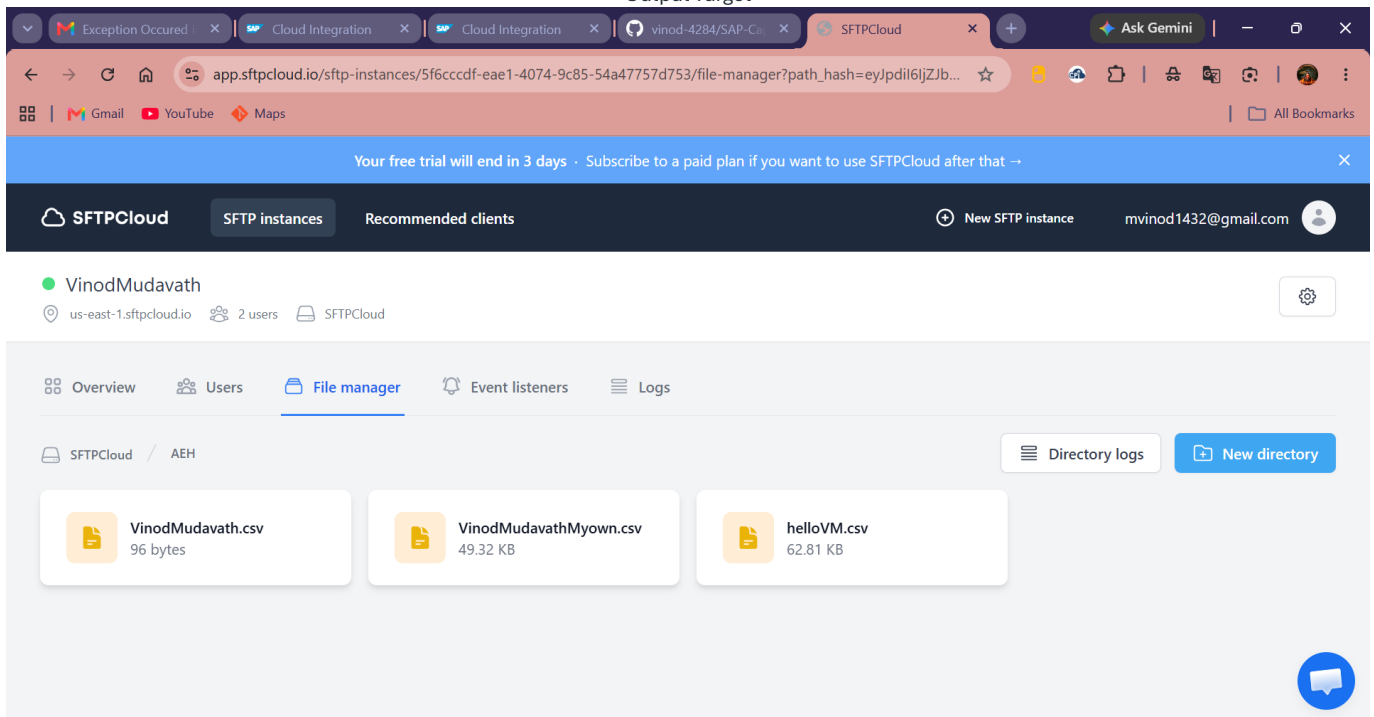

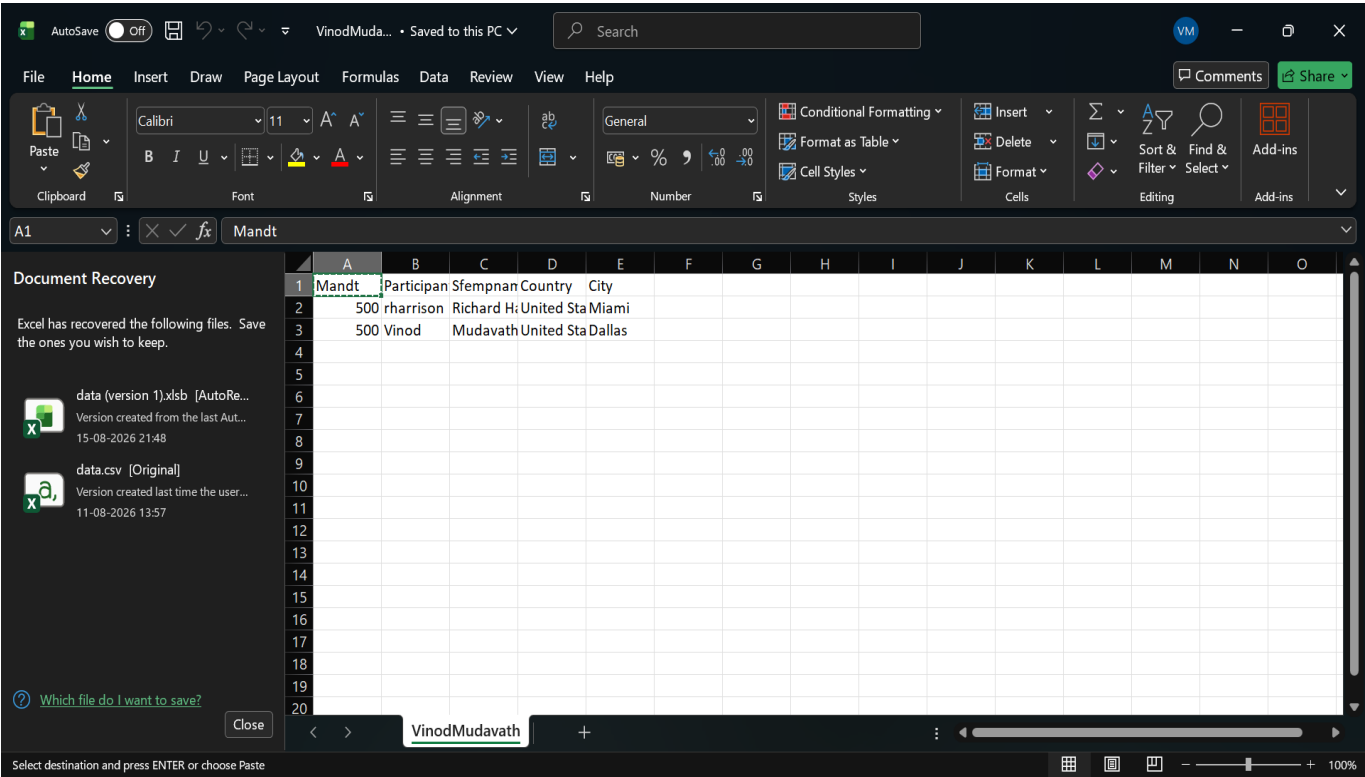

Achieve Target.

13. PROJECT SUMMARY

The project successfully implements an automated employee-data integration solution using SAP BTP Cloud Integration. The integration flow is triggered by a Timer Start event and retrieves employee information from SAP SuccessFactors. The data is mapped to the required S/4HANA structure and used to create employee records in the target system.

The processed employee information is converted from XML to CSV and distributed through SFTP and SMTP/email using Sequential Multicast. An Exception Subprocess handles integration failures and sends appropriate notifications.

Project Outcome Automated integration • Data consistency • Secure distribution • Error handling • Operational monitoring • End-to-end testing

OVERVIEW

Project Outcome



Automated
integration



Data
consistency



Secure
distribution



Error
handling



Operational
monitoring



End-to-end
testing

END OF PROJECT DOCUMENTATION
